



## RAIL KING IR REMOTE CONTROL TEST

The Rail King manual was used to direct the set up and a Rail King Loco Sound Manual which includes the IR Remote.

Fast Track connected, red light is on, and 18 volts from rails. Basic system working.

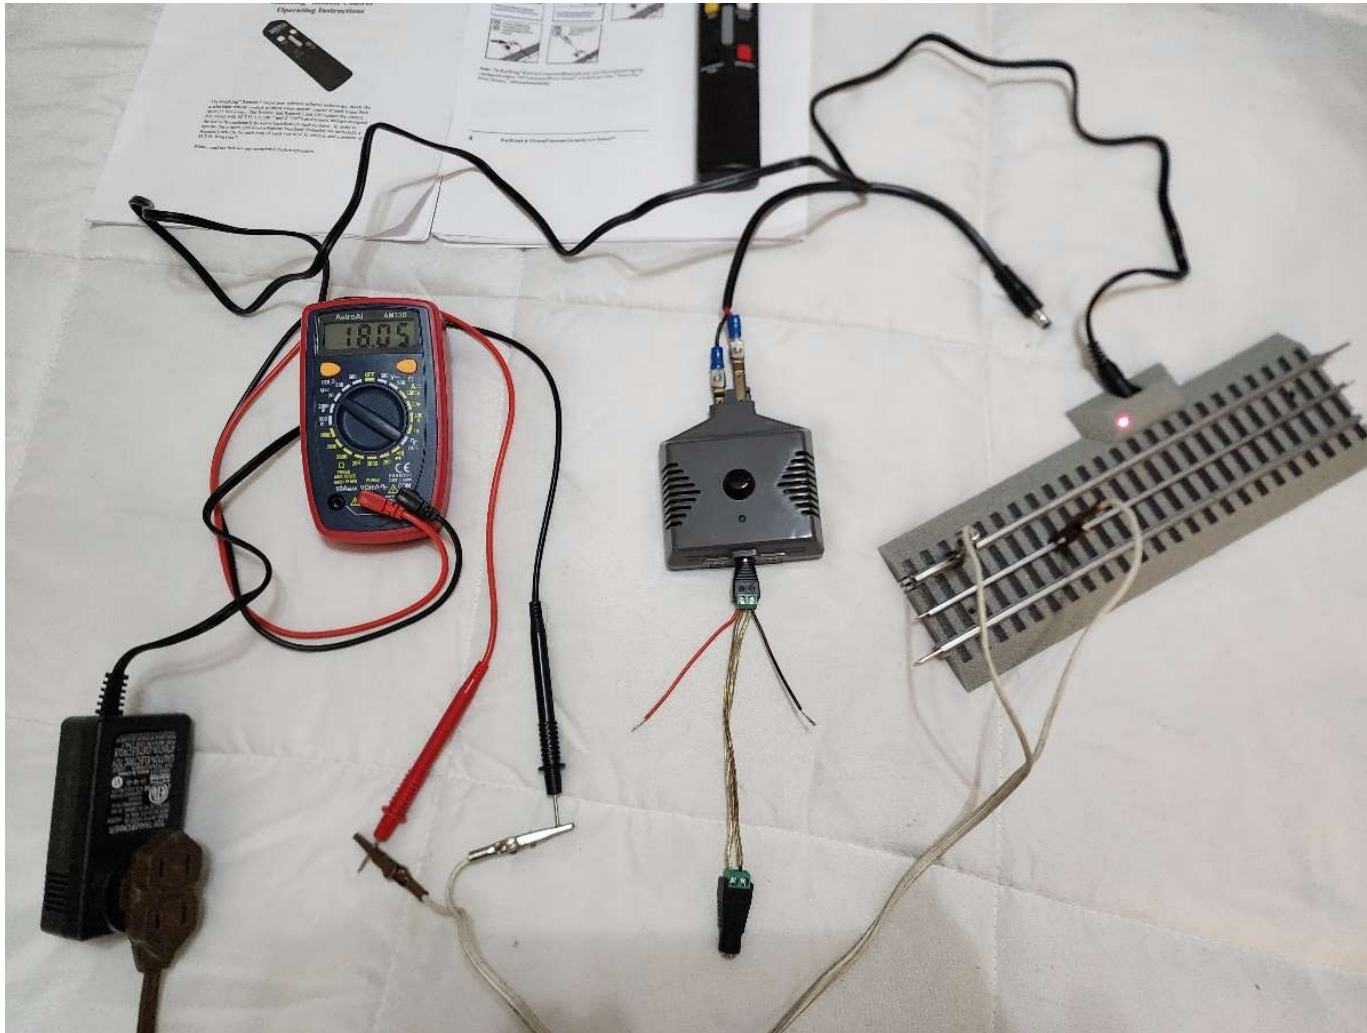

Moved meter to adapter, 2.1 mm x 5 mm, input to Lock-On shows 18 volts from Fast Track Transformer. Remote buttons have not been pressed. Adapter from Lock-On to Fast Track is 2.5 mm x 5.1 mm.

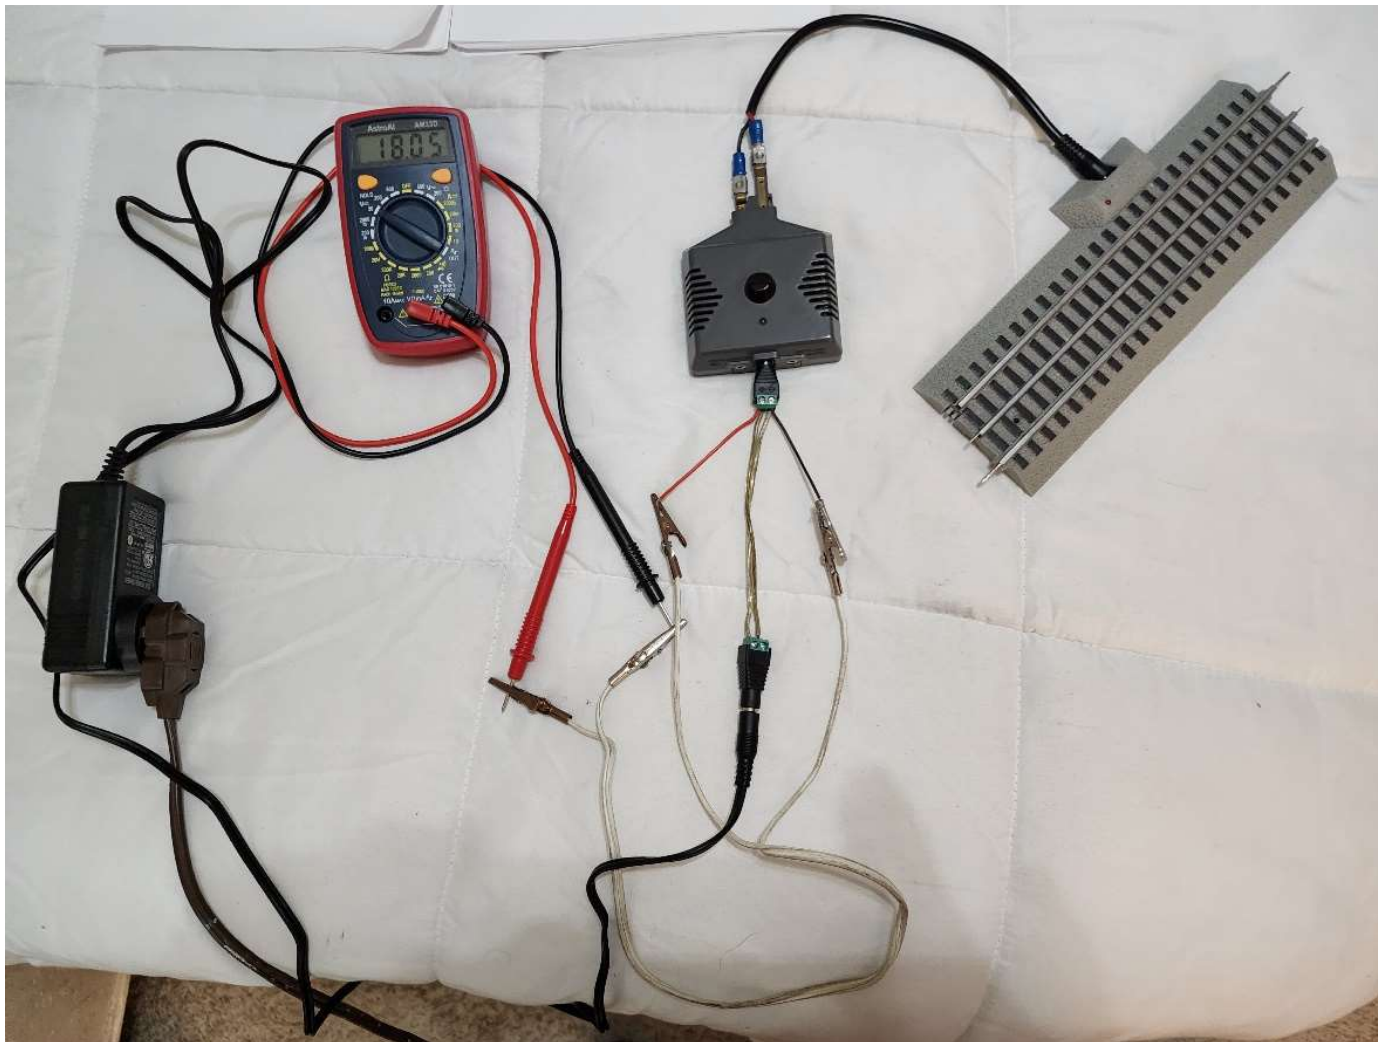

IR Lock-On connected to track, button on IR remote is being pressed, no green light on lock-on and no track voltage. Lock-On is not functional.

IR Remote was tested using a camera on a phone and the IR dot could be seen.

